




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 4D – SR 89A & SR 179 Y Roundabout Bypass Lanes

FY20 CIP Update

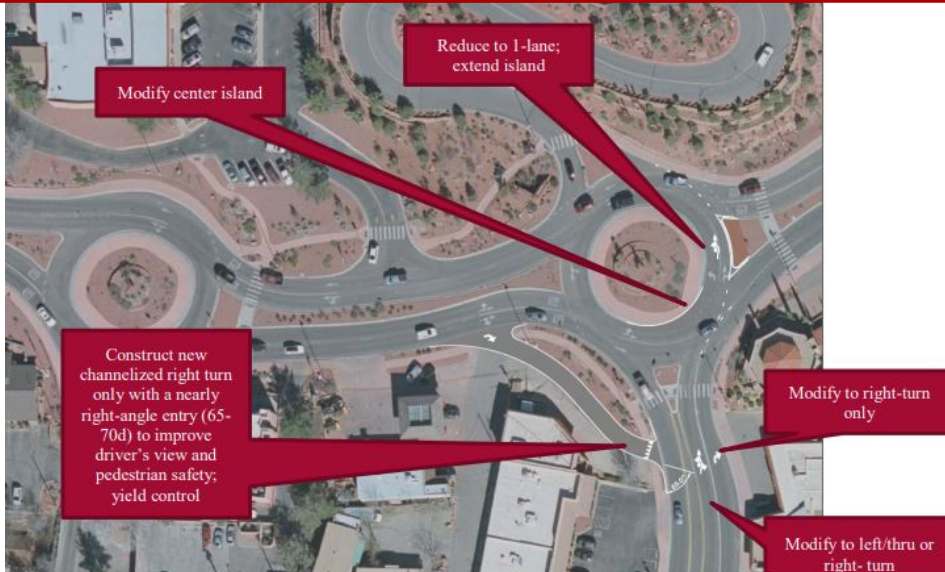

KEY FEATURES:

Consultant: ADOT In-House Design

Contractor: TBD

Timing: July 2018 – FY 22

Construction Challenges:

- Potential land acquisition
- Maintenance of traffic/access
- Maintaining available parking

Project Manager:

Stephen Craver, PE

(928) 203-5059

SCraver@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE

(928) 203-5039

ADickey@SedonaAZ.gov

\$ FY20 Project Budget: \$300,650

Total Project Budget: \$2,392,614

This project is a result of the Transportation Master Plan. The project consists of dedicated right turn lanes toward southbound SR 179, and toward Uptown, at the “Y” roundabout. The turn lanes could be separated from the roundabout by a narrow median. This allows those specific turning movements to bypass the roundabout. The right turns can be made more efficiently because it only requires a merge at the end of the lane rather than a full yield to enter the roundabout, and it also removes those vehicles from the overall capacity of the roundabout. ADOT Northcentral district was awarded competitive district minor project funding, with in-house design starting in FY 19. ADOT will be the lead jurisdiction on the project but the City has committed to contribute 50% of the overall funding. An IGA with ADOT formalizing the City’s contribution was approved at the October 23, 2018 City Council meeting. The IGA was approved by the State Transportation Board on May 17, 2019. A project kick-off meeting, along with a meeting with adjacent property owners and stakeholders, was held on June 3 to get their input about the project. Field survey was completed in July.

Status: Staff is working with ADOT to refine the public involvement plan for the project. The design team is finalizing an alternatives analysis and modeling of various scenarios to minimize parking/access impacts to adjacent properties. The most recent iteration is shown above. A scoping memo is expected to be sent to stakeholders in February 2020. Current anticipation is that construction would start in June 2021.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

December 2019

Project Phase	% Completion	Completion Date
Design	20%	December 2020
Construction	0%	FY22
