




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

WW-01D - WW Collection System Improvements - Misc. Rehabs/Replacements

FY25 CIP Update

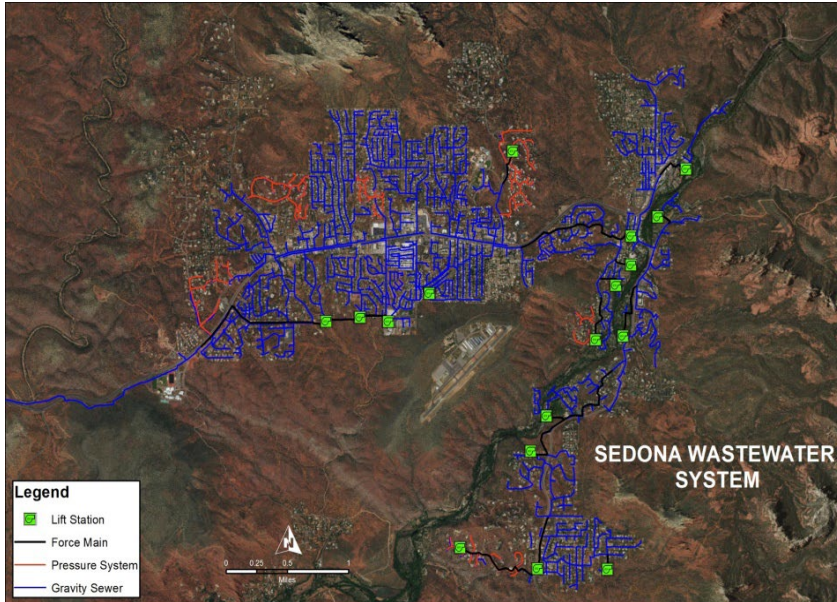

KEY FEATURES:

Consultant: ADC Wastewater Engineering

Contractor: KEAR Civil Corporation

Timing: FY24- FY26

Construction Challenges:

- Potential by-pass operations
- Securing existing services
- Material availability

Project Manager:

Roxanne Holland, PE
 (928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

Kurtis Harris, PE
 (928) 203-5059

KHarris@SedonaAZ.gov

\$ FY25 Project Budget: \$401,000

The 2017 Wastewater Master Plan Update (WWMP) included both condition assessments of existing sewer infrastructure and capacity analysis of the sewer collection system. During the desktop condition assessment, several pipes were identified as having issues such as deteriorated pipe lining, offset joints, cracks in the pipe, and general deterioration from hydrogen sulfide gasses.

This project will install pipe lining in Foothills Drive and El Camino Road, replace a portion of the 6-inch main line in Northview Road, and repair offset joints and re-line the 8-inch mains in Lazy Bear Estates.

Status: Construction of the Northview Sewer Line Replacement project is anticipated to begin on June 2, 2025. Construction crews will begin on the southern end of Northview Rd. and continue north-east. Construction is expected to last 3 months, with completion in early September 2025.

Design for the point repairs in Foothills Drive and El Camino Road is also complete. Staff is looking to have the work completed through a cooperative purchasing agreement beginning this summer.

PROJECT STATUS **MAY FY25**

Project Phase	% Completion	Completion Date
Design	100%	Winter 2023
Construction	0%	Summer 2025
