




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Sedona in Motion 11N - Andante Shared-Use Path & Drainage Imps

FY25 CIP Update

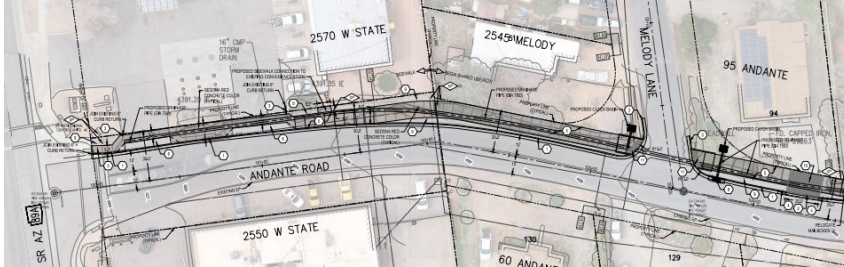

KEY FEATURES:

Consultant: Paradigm Design

Contractor: TBD

Timing: FY23 - FY25

Construction Challenges:

- Limited right-of-way
- Ditches and driveways on both sides
- Lots drain to ditches
- Unpermitted encroachments

Project Manager:

Sandra Phillips, PE, CFM
 (928) 203-5076
SPhillips@SedonaAZ.gov

City Engineer:

Kurt Harris, PE
 (928) 203-5039
kharris@SedonaAZ.gov

\$ FY25 Project Budget: \$1,540,000

The residents of this neighborhood have requested sidewalks and paths for safe pedestrian travel. The Council discussed this project at the retreat as an important project to continue to move ahead as a priority. The GO! Sedona Pathways Plan also lists this as a "Priority Pathway".

Community Outreach meeting occurred in December 2022 at the Sedona Public Library on White Bear Road. Different options were presented to the attendees/residents and participants were asked to identify their preferred option. Bi-lingual door hangers were placed to notify residents of the outreach meeting as well as a letter sent out. The results of outreach showed Andante as the preferred location of the SUP.

Plans are currently at 100% design and Pronghorn Construction has been selected as the lowest bidder. Work to begin late June 2025.

This project will provide a 8ft-10ft wide shared-use pathway connection from Thunder Mountain Road to W SR 89A. This will also provide a multimodal connection between the existing sidewalk on W SR89a and Sanborn Dr. For the latest information please visit:

[Andante neighborhood shared use path | City of Sedona](#)

PROJECT STATUS

MAY FY25

Project Phase	% Completion	Completion Date
Feasibility	100%	FY24
Design	100%	February 2025
Construction	0%	2026
