




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Sedona in Motion 3D - Forest Rd Improvements associated with new Parking Garage FY25 CIP UPDATE

FOREST ROAD IMPROVEMENTS

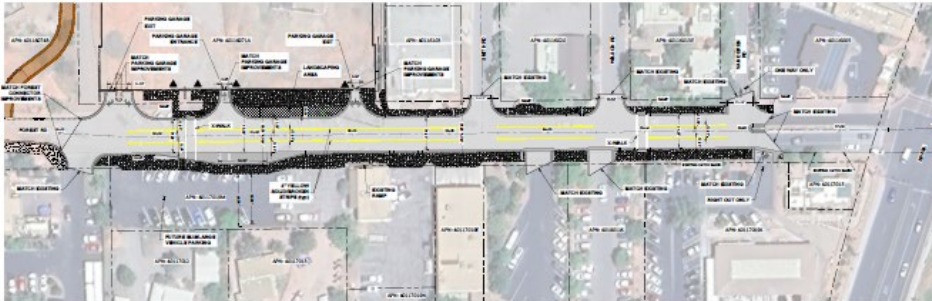

KEY FEATURES:

Consultant: Ardurra Group Inc

Contractor: TBD

Construction Challenges:

Limited Work Area/ Space

Project Manager:

Gillian Arnold
 (928) 203-5109
garnold@sedonaaz.gov

City Engineer:

Kurt Harris, PE
 (928) 203-5059
kharris@SedonaAZ.gov

\$ FY25 Project Budget: \$ 80,000

This project is a result of the Transportation Master Plan to improve the Forest Road Corridor from the property line of the parking garage down to 89A. The goal for this project is to add a shared-use path, shuttle stops, and drainage improvements. This will allow for better pedestrian access to uptown from the parking garage and add additional shuttle stops.

PROJECT STATUS

MAY FY25

Project Phase	% Completion	Completion Date
Design	30%	September 2025
Construction	0%	FY26
